

REQUEST FOR PROPOSAL

Full Design Consultancy Services up to Tender Stage

Abu Dhabi Residential Development Project

Client	UNIESTATE Properties
Project	PLOT C3/RR5, AL REEM ISLAND, ABU DHABI, UAE
RFP reference	UNI/AD/00001
Issue date	11 th MAY 2026
Tender closing date	22 nd MAY 2026
Version	Version 1.0

Contents

1. Invitation to Tender
2. Tender Overview and Instructions
3. Project Outline
4. Scope of Services
5. Design Stage Deliverables
6. Authority Approvals and Regulatory Management
7. Six-Month Market Launch Requirement
8. LDC Team, Subconsultants and Key Personnel
9. Tender Submission Requirements
10. Commercial Proposal Requirements
11. Evaluation Criteria
12. Proposed Appointment Terms
13. Appendices and Templates

Appendix A - Design Brief

Appendix B - Deliverables Matrix

Appendix C - Authority Approval Matrix

Appendix D - Fee Schedule Template

Appendix E - Form of Tender

1. Invitation to Tender

Please see separate letter of Invitation attached.

2. Tender Overview and Instructions

2.1 Definitions

Term	Definition
Client	UNIESTATE
LDC	The successful tenderer appointed as lead design LDC (LDC).
Project	Plot C3/RR5, Al Reem Island, Abu Dhabi.
Authority Approvals	All approvals, permits, no-objection certificates, clearances, stamps, portal submissions and statutory or stakeholder approvals required to progress and tender the design, including master developer approvals.
Market Launch	The Project is to be market ready no later than 6 months from commencement of the design consultancy services. This is a critical milestone and target to effect future funding of the Project.
Tender Stage	A coordinated detailed design package suitable for contractor tendering, cost planning, authority submission/approval and procurement of construction works, subject to any project-specific procurement strategy stated by the Client.

2.2 Tender Programme

Item	Date / Requirement
RFP issue date	11 th May 2026
Tender clarification deadline	19 th May 2026
Site briefing / tender meeting	N/A
Tender submission deadline	22 nd May 2026 – 5pm
Interviews, if required	
Anticipated appointment	5 th June 2026

2.3 Instructions to Tenderers

- Tenderers shall submit separate Technical and Commercial Proposals in PDF format, together with editable schedules in Excel where requested.
- All prices shall be in AED and exclusive/inclusive of VAT as stated in Appendix D. Tenderers shall clearly identify VAT treatment.
- The proposal shall remain valid for 120 days from the tender submission deadline.
- Tenderers shall review the full RFP, site constraints, master developer requirements, authority pathways and all available project information before pricing.
- Any qualifications, exclusions or assumptions must be clearly stated in a single exceptions schedule. Unstated exclusions shall be deemed included.
- The Client may reject non-compliant, conditional, incomplete or late submissions.
- The Client is not obliged to accept the lowest or any tender and may negotiate with one or more tenderers.

2.4 Tender queries

All queries shall be submitted in writing to **Ahmed Sabry** (ahmed.sabri@uniestate.com) by the clarification deadline. Responses may be issued to all tenderers as addenda.

3. Project Outline

3.1 Project Description

- Please refer to Appendix A, Design Brief for the development project details, description and Client's requirements.

3.2 Client Objectives

- Create a commercially viable development that responds to market demand, plot constraints, authority requirements and the Client's return objectives.
- Produce a coordinated, tender-stage design package covering architecture, engineering, landscape, external lighting, wayfinding and signage.
- Achieve a market-ready launch package within six months of appointment as a condition of the Client's bank funding arrangements.
- Obtain and manage all master developer, statutory and utility approvals required up to tender stage, or provide documented evidence of submissions, authority comments, approvals status and no-objection path where an authority review period extends beyond the six-month launch gate.
- Minimise redesign risk by securing early authority and master developer engagement, especially for massing, planning parameters, traffic, utilities, fire/life-safety, Estidama and public realm interfaces.
- Maintain design quality, saleability, efficiency, technical compliance and cost certainty through each stage gate.

3.3 Critical Milestones

Milestone	Deliverable / Gate	Required timing
M0	Appointment / Notice to Proceed	Day 0
M1	Inception, project controls, authority approval route map and information request	Within 10 working days
M2	Pre-concept massing options and comparative recommendation	Within 4 weeks
M3	Preferred concept design and launch-area strategy	Within 8 weeks
M4	Schematic design and authority / master developer submission package	Within 14 weeks
M5	Detailed design freeze for market launch, bank/funder pack and draft tender documentation	Within 20-22 weeks
M6	Market-ready launch package and tender-stage issue pack	No later than six months from appointment

Tenderers shall submit a realistic, resource-loaded programme that demonstrates how these milestones will be achieved, including authority review periods, master developer response periods, dependencies, assumptions and recovery measures.

4. Scope of Services

4.1 Appointment Scope

The LDC shall provide full lead design consultancy services for the Project from appointment through pre-concept/massing options, concept design, schematic design and detailed design up to tender stage.

The LDC shall be responsible for all design coordination, design management, technical integration, authority strategy, authority submissions, master developer approvals and design documentation necessary to achieve the Client's objectives and the six-month market-launch milestone.

Unless otherwise agreed, the LDC scope shall include the appointment, management and coordination of all design and engineering disciplines necessary to deliver a complete, coordinated and authority-compliant design for the Project. No gaps in scope between disciplines will be accepted.

The LDC shall coordinate with the Client's project manager, cost manager, commercial/marketing advisors, legal advisors, bank/funder advisors and any other consultants appointed by the Client.

4.2 Core Disciplines

- Architecture and lead design management.
- Urban design, massing, development optimisation and planning compliance.
- Structural engineering, including foundation strategy and coordination with geotechnical inputs.
- Civil engineering, infrastructure, roads/access, grading, drainage, stormwater, utilities coordination and enabling works interfaces.
- Mechanical, electrical and plumbing engineering, including plant space planning, utility loads, energy strategy, fire/life-safety interfaces, vertical transportation and specialist systems as required.
- Fire and life safety strategy, including coordination with Abu Dhabi Civil Defence, or approved fire LDC where required.
- Landscape architecture, hardscape, softscape, irrigation, shade, furniture, public realm and amenity design.
- External lighting design, including landscape, facade, public realm, parking, access and signage lighting interfaces.
- Wayfinding and signage strategy and design, including statutory, vehicular, pedestrian, parking, development identification, bilingual Arabic/English and master developer signage requirements.
- Facade design, envelope performance and material strategy, where required for the asset class.
- Sustainability / Estidama Pearl Rating services, including Pearl Qualified Professional support, where required.
- Traffic / transport planning, access, parking, circulation and interface with ITC / relevant roads authorities where required.
- Environmental permitting support, including PER/EIA/CEMP interface, where required.
- BIM / CAD management, clash coordination and data outputs.
- Any further specialist services required for approvals, tender-stage design or market launch, including acoustics, security, waste management, district cooling, gas, telecoms, retail planning, or accessibility, as applicable.
- Marketing collateral production, sales brochures, animations, sales centre design, physical models and final CGIs, and other base information required for market launch.
- Interior design, FF&E and operator technical services, unless stated in the Project brief.

4.3 LDC Responsibilities

- Act as single point of responsibility for the design team and all subconsultants.
- Prepare and maintain the design management plan, deliverables schedule, approvals matrix, risk register, assumptions register and interface matrix.
- Coordinate all disciplines so that drawings, schedules, reports, models and specifications are complete, consistent and tenderable.
- Coordinate and incorporate cost consultant feedback, value engineering and Client commercial decisions without compromising authority compliance or the launch milestone.
- Prepare, sign, stamp, submit, track, respond to and close authority comments for all submissions within the LDC's scope.
- Attend weekly Client meetings and authority / master developer meetings as required.

- Provide weekly progress reports, including decisions required, design status, approvals status, risks, lookahead and recovery actions.
- Maintain a live document register, decision log, RFI log and approvals tracker.
- Maintain and disseminate minutes of all design team meetings and live actions tracker.
- Provide all native files, editable source files and models required by the Client, funder, cost consultant or tender process.
- Provide cloud based electronic document management system (EDMS) with collaborative properties with access given to the client, project manager, and cost manager, free of charge for the duration of the contract.
- Maintain comprehensive document registers throughout with strict version control. Registers must be exhaustive of all documents in respect of each discipline.

4.4 Exclusions and Optional Services

The following services are excluded only if the tenderer expressly lists them in its proposal and the Client accepts the exclusion in writing. Otherwise, services necessary to deliver the RFP objectives are deemed included.

- Construction supervision / supervision services after award of the works contract.
- Post-tender contractor shop drawing review and construction stage services.
- Independent cost consultancy / bills of quantities, unless the LDC is expressly appointed to provide QS services.
- Topographical survey, geotechnical investigations, traffic counts, environmental baseline surveys and utility detection surveys, unless included in the LDC's fee proposal.

Tenderers shall provide optional prices for any excluded or optional services in Appendix D.

5. Design Stage Deliverables

The LDC shall provide the deliverables below as a minimum. Tenderers may propose additional deliverables where necessary to achieve the Client's objectives, market-launch milestone or approval requirements.

5.1 Inception and Project Controls

- Kick-off workshop and stakeholder map.
- Review of all Client information, plot documents, affection plan, title/lease documents, master developer guidelines, surveys, utility records and prior approvals.
- Information request schedule with required dates and criticality.
- Design management plan, communications protocol, CDE/BIM strategy, deliverables schedule and programme baseline.
- Authority Approval Route Map issued within 10 working days, including master developer pathway, statutory pathway, review durations, dependencies and risk register.
- Site visit report with photographic records and key constraints.

5.2 Pre-concept /Massing Options

- Minimum [three] massing and development options unless otherwise agreed.
- Planning parameter review: land use, height, setbacks, GFA, FAR, parking, access, easements, rights of way, utilities, fire access, public realm and master developer controls.
- Option plans, sections, 3D massing and building orientation, indicative unit mix, area schedule, efficiency analysis, parking yield, access strategy and high-level engineering feasibility.
- Commercial and marketability assessment in coordination with Client advisors, including saleable area, view corridors, amenity positioning, phasing and premium value opportunities.
- Authority risk review for each option, including likely comments and approval risk.
- Recommendation report identifying preferred option, design risks, approvals strategy and decisions required.

5.3 Concept Design

- Preferred concept design for Client approval and pre-application engagement with master developer and key authorities.
- Concept layout plans, elevations, sections, 3D views, plot integration, access/circulation, preliminary facade approach and material intent.
- Concept landscape, public realm, external lighting and wayfinding/signage strategies.
- Structural concept, MEP concept, utility load estimates, civil/infrastructure concept, fire/life-safety strategy and parking/traffic strategy.
- Interior design for units, common areas and amenities.
- Estidama / sustainability strategy, target Pearl rating, required credits, energy/water approach and PQP plan.
- Updated area schedule and launch feasibility pack for Client commercial review.
- Concept design report and presentation deck.

5.4 Schematic Design

- Coordinated schematic design drawings for all disciplines, including interior designs.
- Structural grid, preliminary member sizing, foundation strategy and coordination with geotechnical assumptions.
- MEP plant rooms, risers, shafts, ceiling zones, service routes, utility connection strategy and preliminary calculations.
- Landscape layout, grading, irrigation approach, planting palette, hardscape, furniture, shade and public realm interfaces.
- External lighting layouts, preliminary lux strategy, control philosophy and coordination with landscape and signage.
- Wayfinding and signage hierarchy, sign family, location principles and approval interface.
- Traffic, access and parking report as required by authorities.
- Authority submission packages for master developer and statutory authorities as applicable.
- Updated cost-plan coordination package and value engineering responses.
- Schematic design report, risk register and design decision log.

5.5 Detailed Design / Tender-stage Design

- Fully coordinated detailed design drawings, schedules, specifications and reports for all disciplines, suitable for contractor tendering.
- Tender-stage architectural package including plans, elevations, sections, details, room/unit schedules, door/window schedules, facade intent and material schedules.
- Tender-stage structural, MEP, civil/infrastructure, landscape, lighting, wayfinding/signage and specialist packages.
- Authority drawings, forms, calculations and reports required for building permit and associated approvals.
- Design risk register, specifications, design criteria, outline construction methodology constraints and interface schedule.
- BIM model / coordinated model and clash report where BIM is required.
- Technical tender clarifications support during the tender period if included in the appointment.
- Final market-launch design pack, bank/funder pack and approvals status report by the six-month milestone.

5.6 Deliverables - Format Requirements

- PDF packages suitable for Client approval and authority submission.
- Native CAD/Revit/BIM files, IFC, Navisworks or other agreed formats where applicable.
- Editable Word, Excel and PowerPoint files for reports, schedules and presentations.
- Area schedules in Excel with formulas visible and assumptions clearly stated.
- Drawing registers, revision history and transmittals for every issue.
- Separate "Client approval", "authority submission", "market launch" and "tender issue" packages, where required.

6. Authority Approvals and Regulatory Management

6.1 LDC Responsibilities

The LDC shall be responsible for identifying, programming, preparing, coordinating, submitting, tracking, responding to and obtaining all authority approvals required for the design services up to tender stage. This includes the relevant master developer approvals and all statutory, municipal, utility, safety, environmental, transport, sustainability and stakeholder approvals applicable to the Project.

- The LDC shall not rely on generic authority assumptions. The approvals pathway must be project-specific and must reflect the plot, master development, jurisdiction, asset class, phasing and procurement strategy.
- The LDC shall maintain a live Authority Approval Matrix from inception to completion, updated weekly.
- The LDC shall identify critical approvals that could affect the six-month launch milestone and shall propose mitigation, early engagement and parallel submission strategies.
- The LDC shall attend authority and master developer meetings, workshops, pre-application reviews and comment resolution sessions.
- Authority comments arising from inadequate, incomplete, uncoordinated or non-compliant LDC submissions shall be addressed without additional fee or extension of time.
- Client approval of a design stage shall not relieve the LDC of responsibility for authority compliance, coordination or technical adequacy.

6.2 Authority Approvals

- Provide an Authority approvals roadmap within 10 days of appointment.
- Confirm the controlling jurisdiction and approval route: mainland municipality / master developer / free zone / ADGM / special district / other.
- List all anticipated approvals and NOCs, including master developer (Modon/Najmat), ADM/DMT/TAMM, planning/DPA, building permit, Estidama, AD Civil Defence/fire-life-safety, traffic/roads, ADDC/utilities, gas, sewerage, stormwater, irrigation, district cooling, Etisalat/Du/telecom, waste, environment, aviation/height, heritage/cultural and signage/advertising as applicable.
- Identify required portal access, LDC registration/classification, signatories, stamps, powers of attorney, appointment letters and Client documents.
- Identify information required from the Client and third parties.
- Set out submission sequence, dependencies, authority review durations, expected comment cycles, decision points and float.
- Identify approvals required for market launch, approvals required for tender issue and approvals that may continue beyond launch if permitted by the Client and funder.
- Provide a risk-rated approvals programme and mitigation plan.

6.3 Indicative Authorities and Stakeholders

The list below is indicative and not exhaustive. Tenderers shall complete and validate it for the Project.

Authority / Stakeholder	Typical interface	LDC Obligation	Timing
Master developer / estate management	Plot compliance, design guidelines, interface, design NOC, phasing and community rules.	Prepare submissions, resolve comments and secure NOC/approval.	Pre-concept onward.
DMT / ADM / TAMM / MePS	Project registration, planning/building permit submissions, certified drawings, municipal comments.	Manage all submission packages, responses, resubmissions and evidence of approval.	Inception onward.
Planning / DPA route where applicable	Detailed Planning Approval, circulation plan, land use and development controls.	Confirm applicability and secure approval	Concept / schematic.

		or required status evidence.	
Estidama / Sustainable Buildings	Pearl Design Rating, sustainability compliance, energy/water credits.	Provide PQP and documentation; integrate credits into design.	Concept through tender.
AD Civil Defence / fire-life-safety	Fire strategy, life safety, fire alarm/fighting, emergency access.	Coordinate strategy and secure required review/approval.	Concept through tender.
ITC / traffic / roads authority	Access, parking, traffic impact, road interfaces, construction traffic constraints.	Prepare traffic studies and submissions where applicable.	Pre-concept through schematic.
Utilities and infrastructure providers - ADDC	Power/water, sewerage, stormwater, irrigation, district cooling, telecoms, gas and diversions.	Loads, applications, NOCs, drawings, calculations and coordination.	Concept through tender.
Environment Agency - Abu Dhabi / environmental authorities	PER, EIA, CEMP, environmental permits, sensitive receptors.	Screen applicability, appoint specialists if required and secure approvals.	Early concept onward.
Waste / Tadweer or relevant waste authority	Waste strategy, bin rooms, collection access, C&D waste requirements.	Coordinate design and submissions as applicable.	Concept / schematic.
DCT / heritage / cultural authority	Archaeology, cultural assets, heritage constraints if applicable.	Screen site and secure NOC if required.	Pre-concept.
Aviation / height / security authorities	Height restrictions, cranes, flight path, CCTV/security requirements if applicable.	Screen and obtain clearances as required.	Pre-concept through detailed design.
Signage / advertising / public realm stakeholders	External signage, wayfinding, development identity, Arabic/English content, lighting.	Integrate with master developer and municipal approvals.	Schematic / detailed design.

6.4 Authority Fees

Unless otherwise stated, statutory authority fees and third-party application charges shall be paid by the Client at cost against official receipts. The LDC shall include all professional time, coordination, preparation, submission, resubmission and follow-up costs in its lump sum fee. No additional fee shall be payable for resubmissions caused by LDC error, omission, lack of coordination or non-compliance.

6.5 Reporting

- Weekly approvals tracker showing each authority, submission date, status, comments, next action, owner, due date, risk and impact on the six-month milestone.
- Copies of all submission receipts, portal screenshots, authority comments, meeting minutes, responses and approvals.
- Monthly approvals dashboard for Client and funder reporting.
- Immediate escalation of any approval risk that may affect launch, funding, tender issue, cost or scope.
- Design team and stakeholder meeting minutes and live actions tracker.

7. Market Launch Requirement

The LDC acknowledges that the Project must be ready for a market launch within six months of appointment. This is a critical condition linked to the Client's bank funding requirements.

7.1 Required Launch Deliverables

- Approved or Client-endorsed development concept and schematic design status sufficient for launch, funding due diligence and market communication.
- Coordinated area schedule with GFA, BUA, NLA/NSA/SLA, unit areas, sellable areas, parking, amenities and reconciliation against authority definitions and master developer requirements.
- Plans, typical unit layouts, key elevations, sections, massing views, landscape/amenity strategy and public realm interfaces suitable as source information for marketing collateral.
- Launch design control pack, including rendered architecture, amenities and unit layout plans, area schedules and room sizes. Plus, any other material determined in conjunction with the Clients marketing and branding team.
- Authority approvals status report, including approvals obtained, submissions made, comments pending, anticipated approval dates, risks and mitigations.
- Bank/funder technical pack: design summary, programme, approvals status, risk register, design responsibility matrix, supporting cost plan information and LDC duty-of-care inputs as required.

7.2 Launch Governance

The LDC shall support weekly launch-readiness reviews from completion of the concept design stage until launch. The LDC shall flag any design decision, authority dependency, Client information delay or third-party issue that could affect launch and shall propose a recovery plan within three working days of identifying the risk.

The Client may require the LDC to execute a duty of care letter or collateral warranty in favour of the bank/funder and/or project company.

8. LDC Team, Subconsultants and Key Personnel

8.1 Minimum Team Requirements

- Lead Design Director / Principal-in-Charge with authority to allocate resources and resolve issues.
- Lead Architect and discipline heads for architecture, structure, MEP, civil/infrastructure, landscape, external lighting, wayfinding/signage and sustainability.
- Authority Approvals Manager with demonstrable Abu Dhabi experience, including master developer and DMT/municipality processes.
- BIM/CAD Manager and document controller.
- Specialists for fire/life-safety, traffic, environmental, facade, district cooling, gas, telecoms, vertical transportation or other services where required.
- Registered engineers and classified entities required to submit and stamp drawings in Abu Dhabi.

8.2 Tender Submission Evidence

- Organisation chart showing prime LDC, subconsultants, reporting lines and named individuals.
- CVs for all key personnel, including relevant Abu Dhabi project approvals experience.
- Trade licences, DMT/TAMM classification or registration evidence and engineer registration cards where applicable.
- Subconsultant appointment letters or letters of commitment.
- Availability statement confirming named resources are committed to the six-month programme.
- Professional indemnity and insurance certificates.
- Quality management, BIM and document control procedures.
- Three to five comparable project case studies, including approvals achieved, master developer interface and delivery period.

8.3 Replacement of Key Personnel

Key personnel may not be replaced without the Client's prior written approval. Any replacement shall have equal or better qualifications, experience and immediate availability. The LDC shall not reallocate key personnel in a manner that jeopardises the six-month launch milestone.

9. Tender Submission - Requirements

9.1 Technical Proposal

- Executive summary and confirmation of compliance with the RFP.
- Understanding of the Client's objectives, commercial drivers, bank funding requirements and six-month launch deadline.
- Design methodology for pre-concept/massing, concept, schematic and detailed/tender design stages.
- Project-specific authority approvals strategy and preliminary Authority Approval Matrix.
- Resource-loaded programme with critical path and recovery measures.
- Team structure, CVs, registration/classification evidence and subconsultant's details.
- Comparable experience, especially Abu Dhabi development projects with master developer and authority approvals.
- QA/QC, BIM/CAD, coordination and document control methodology.
- Risk register covering design, approvals, programme, market launch, cost, procurement and stakeholder risks.
- Assumptions, exclusions and information required from Client.
- A valid certificate of business registration in Abu Dhabi via an Emirate approved legal entity or evidence of forthcoming registration directly or through business association.

9.2 Commercial Proposal

- Lump sum fee payable by stage.
- Resource schedule showing role, person, discipline, hourly/day rate, planned hours/days and stage allocation.
- Reimbursables and disbursements, if any, with caps and approval requirements.
- Authority fees and third-party costs schedule, identifying whether excluded, provisional or included.
- Optional services and rates.
- Payment milestones tied to accepted deliverables and authority/launch milestones.
- Commercial clarifications and exceptions to the proposed appointment terms.
- Confirmation of VAT registration, treatment and validity period.

9.3 Mandatory Schedules

- Appendix A – Design Brief
- Appendix B - Deliverables Matrix compliance.
- Appendix C - Authority Approval Matrix completed by tenderer.
- Appendix D - Fee Schedule and Resource Schedule.
- Appendix E - Compliance Statement.
- Appendix F - Signed Form of Tender.

10. Commercial Proposal - Requirements

The tender fee shall be a fixed lump sum for all services required to deliver the Scope of Services unless expressly agreed otherwise by the Client. The LDC shall include all management, coordination, design, authority, meetings, reporting, QA/QC, subconsultants and submission costs required up to tender stage.

10.1 Fee breakdown

Stage	Architecture / Lead	Engineering	Specialists	Total Fee AED
Inception and approvals route map	[AED]	[AED]	[AED]	[AED]
Pre-concept / massing options	[AED]	[AED]	[AED]	[AED]
Concept design	[AED]	[AED]	[AED]	[AED]
Schematic design	[AED]	[AED]	[AED]	[AED]
Detailed / tender design	[AED]	[AED]	[AED]	[AED]
Authority submissions and approvals management	[AED]	[AED]	[AED]	[AED]
Market launch / bank funding pack	[AED]	[AED]	[AED]	[AED]
Tender support optional	[AED]	[AED]	[AED]	[AED]
Other optional services	[AED]	[AED]	[AED]	[AED]

10.2 Payment Principles

- Payment shall be linked to accepted deliverables, not mere issue of documents.
- The Client may retain [10%] of each invoice until the relevant stage deliverables and submissions are accepted.
- Authority fees shall be reimbursed at cost only where approved in advance and supported by official receipts.
- No additional payment shall be made for correcting LDC errors or responding to authority comments caused by incomplete or uncoordinated submissions.
- Variations require prior written approval by the Client.

11. Evaluation Criteria

The Client intends to evaluate proposals using the indicated criteria and weighting below. The Client may amend the weighting or apply additional pass/fail requirements prior to Tender submission date.

Criterion	Weighting	Key Considerations
Technical: approvals strategy	12%	Project-specific route map; Abu Dhabi authority experience; master developer pathway; risk and mitigation.
Technical: relevant experience	11%	Comparable Abu Dhabi projects, design-to-tender, approvals and fast-track delivery.
Technical: design methodology	12%	Commercial, market-ready, coordinated design approach across stages.
Technical: team and resources	10%	Based upon experience, qualifications, quality of subconsultants, registrations, and availability.
Technical: QA/QC, BIM and deliverables	5%	Coordination controls, model strategy, document quality and tender readiness.
Commercial: Commercial terms and conditions, form of Agreement	15%	Cost, marketability, authority and funding risk management.
Commercial: lump sum fee, rates and deliverables schedule	25%	Competitiveness, value and alignment with scope.
Commercial: transparency and resources	10%	Clear fee build-up, adequate hours and discipline coverage.

12. Proposed Appointment Terms

The appointment shall be based on the LDC's standard form of Agreement, a copy to be included within the Tender submission.

Topic	Outline Terms
Standard of Care	The LDC shall exercise the reasonable skill, care and diligence expected of a properly qualified, experienced and competent lead design LDC carrying out comparable projects in Abu Dhabi, subject to any higher express obligations stated in the appointment.
Time Obligations	Time is of the essence for the six-month market launch milestone if stated in the final appointment. The LDC shall proactively manage resources and recovery actions.
Approvals	The LDC is responsible for complete, coordinated and compliant submissions and for managing the approvals process. Authority decision times are not guaranteed, but the LDC remains responsible for programming, follow-up, resubmissions and mitigation.
Professional Indemnity	The LDC shall provide and maintain a minimum professional indemnity insurance of not less than AED50 million for each claim during and after completion or as required by the Client/funder.
Intellectual Property	The Client shall receive an irrevocable, royalty-free license to use, copy, modify and develop the design and deliverables for the Project, including for funding, marketing, tendering, construction, operation and future modifications. Consider whether full assignment is required.
Funder Reliance	The LDC shall provide reasonable reliance letters, duty of care letters or collateral warranties to the Client, project company, funder and master developer if required.
Confidentiality	All project information, launch strategy, bank requirements, pricing and design information are confidential.
Subconsultants	The LDC remains fully responsible for subconsultants as if their services were performed by the LDC.
Change Control	No additional fee or time shall be due unless a Client-instructed change materially changes the scope and is agreed in writing.
Termination	The Client may terminate for convenience or default in accordance with the appointment. The LDC shall provide all work-in-progress and native files on termination.
Governing law	The appointment shall be governed by the laws of Abu Dhabi / UAE Federal laws as applicable, with disputes resolved by ADGM Courts / Abu Dhabi Courts / arbitration as inserted by legal counsel.

13. Appendices and Templates

The following appendices are intended to be issued with the RFP and completed by tenderers where applicable.

Appendix A – Design Brief

Introduction

This brief sets out the client requirements, project objectives, base development data, quality expectations, and consultant deliverables for the proposed residential tower on Plot C3/RR5, Reem Island, Abu Dhabi. It is intended to form part of the RFP package for the appointment of a Lead Design Consultant(LDC) to deliver full design services up to tender stage.

The brief should be read together with Annex A: Land and Title Information; and Annex B: Najmat Master Developer Control Plan.

Project Summary

Project/Plot	C3/RR5		
Location	Reem Island, Abu Dhabi		
Development Type	Residential high-rise tower		
Building Form	P5+30	Project BUA	47,563 sqm
Plot area	3,087 sqm	Residential GFA	32,900 sqm
Assumed Residential NIA	27,965 sqm	Indicative unit count	228 units

Intended Consultant Appointment

The LDC shall provide full multidisciplinary design services, coordinate the required sub-consultants, and develop the project through concept, schematic / developed design, statutory submissions and tender documentation.

The design services and deliverables should include as a minimum:

- Pre- concept option and massing studies
- Concept design and design narrative.
- Schematic design including final layouts
- Authority submission coordination, and design optimisation.
- Detailed design to support full tender documentation.
- Interior designs, sufficient for sales and marketing launch
- Coordination of architecture, structure, MEP, vertical transportation, façade, fire/life safety, sustainability, landscape, signage, lighting and other required disciplines.
- Preparation of outline and detailed specifications, schedules, room data requirements, and tender drawings.
- Tender support, technical clarifications, and tender evaluation support.

Project Vision and Positioning

The development is intended to be a contemporary high-rise family orientated residential product designed for a premium but commercially attractive market position. The LDC is expected to respond to both the commercial requirements and the residential product aspirations set out in this brief. These include:

- Create a stylish residential address evoking a calm, light and contemporary aesthetic.
- Prioritise livability through generous glazing, use of daylight, efficient room planning, meaningful storage, and seamless connection to balconies and views.
- Balance premium features with commercially realistic construction, maintenance and operating choices.
- Provide a coherent resident arrival and amenity experience that enhances sales and long-term value.
- Deliver efficient planning and good internal functionality but with a feeling of home.
- Introduce creative ideas and practical solutions for utilisation of small spaces.
- Integrate smart-home technology throughout the development.
- Energy saving devices are to be included to minimize living costs for residents.
- Create an environment that provides comfort, convenience and enjoyment for the residents.
- Help the client to define some unique USPs in terms of product and amenity.
- Develop a well-coordinated and buildable design package suitable for tendering.

Site, Planning and Statutory Context

- The LDC should review and incorporate all plot constraints, set-backs, rights-of-way, utility easements, access restrictions, authority processes and master developer requirements affecting the site.
- Abu Dhabi statutory requirements shall be treated as a core design driver from the date of appointment.
- Building permit and code compliance in Abu Dhabi are administered through Department of Municipalities and Transport, including the BINAA / digital permit ecosystem and the associated smart library of construction regulations.
- The design shall satisfy applicable Abu Dhabi municipality requirements, plot-specific planning controls, and all current code and permit submission requirements in force at the time of design and submission.
- Applicable Estidama / Pearl Building Rating System requirements and submission templates shall be incorporated into the design and authority strategy from the outset.
- Fire and life safety design shall comply with the current UAE Fire and Life Safety Code of Practice and Abu Dhabi Civil Defence review / approval requirements.
- All utility provider compliance requirements for power, water, drainage, telecoms and gas (if adopted) shall be integrated into the design development and authority submission strategy.

Accommodation Schedule

The latest uploaded workbook sets out the current working area and accommodation data summarised below. The architect shall validate these metrics during concept design and issue a fully coordinated controlled area schedule separating plot areas, GFA, GIA / NSA, saleable area, balcony areas, parking, BOH and amenity allocations.

Description	Area	Source / basis	Comment
Plot area	3,087 sq m	Title Document	Check against title and survey.
Residential GFA	32,900 sq m	Affection Plan	Current design brief target.
Residential NIA	27,965 sq m	Client feasibility	Based on 85% gross-to-net assumption for the residential tower
Podium Parking Area	14,663 sq m	Client feasibility	Indicates 5 podium levels. No basement.
Typical Floorplate/floors	1,080 sq m / approx 30 floors	Client feasibility	To be tested against tower efficiency and core design.

Unit Type	Average Unit Size (sqm)	Indicative No of Units	Indicative NIA (sqm)	Briefing Note
1 Bed	70	60	4,195	Premium unit (80sqm)incl study/box room with guest. Standard unit (65 sqm)
2 Bed	110	89	9,788	Premium unit incl maids room; 2.5 bathroom plus, guest w/c. Standard unit, no maid, sep laundry
3 Bed	180	51	9,228	Subject to typology development.
Townhouses (3 Bed)	180	16	2,796	Subject to typology development.
Duplex (3 Bed)	160	12	1,958	Subject to typology development.

All units to provide balconies, except at podium level. An allowance of 15% of GIA has been allocated for balconies. (GIA + 15% = Unit GFA).

It is envisaged townhouses will be distributed on the perimeter of the podium roof level with internal gardens.

Duplexes will face the town houses on the first two accommodation floors of the tower with access to gardens, where possible.

Amenities and Shared Facilities

The following amenities should be incorporated into the design as a minimum, subject to validation of area, structural loading, operational practicality, life safety, servicing and master developer / authority acceptability.

The client intends for the development to provide a home from home feel throughout.

Amenity	Indicative Location	Briefing Note
Kids pool/play area	Podium	Integrate with family zone and passive supervision.
BBQ area	Podium	Provide shade, seating and family use strategy.
Clubroom/co-work/entertainment	Roof	Premium shared resident space.
Indoor play	Podium	Family amenity near podium leisure uses.
Adult pool	Roof	Roof amenity subject to structural and privacy review. Some shade. Incl sunbathing deck.
Gym/studio	Roof	Coordinate with wellness provider and ensure there are segregated changing facilities.
Paddle court	Podium	Validate dimensions, acoustics and weather protection.

Retail	TBC	Extent and requirement to be confirmed.
Other	TBC	Consideration to be given to suggestions and ideas for additional amenities.

Bearing in mind the recent conflict in the Gulf region it would be prudent to consider a safety/evacuation zone within the building.

Amenities on the podium should be accessible from common area corridors directly onto the outside space or via the indoor playroom.

The amenities will be managed and maintained by the Client's FM team. Specialist service providers will be used to provide some specialist health and fitness services.

Car Parking, Access and Servicing

- Based on the proposed unit mix and count, approximately 396 no car parking spaces are required. This assumes a provision of 1 space per 1-bedroom unit, 2 spaces per 2-bedrooms and above, plus an allowance for visitors. The podium is anticipated to be over 5 levels with parking entrances and servicing to be from the ground floor. There will be an efficient ramp system to the upper floors. The podium should be cladded in a style complimenting the main building and pleasing to the eye at street level. Attention to the lighting detail and logo/branding should be considered at concept design stage.
- Service access and routes should be shared or integrated wherever possible or permissible, according to local regulations and codes. Vehicular access areas should be segregated and clearly signposted with a separate pedestrian/resident's route and wayfinding signage.
- The main pedestrian entrance and lobby for the building at street level should be clearly independent of vehicular access and car parking entrances.
- The LDC will need to assess the following client considerations within the design and car parking arrangement:
- Develop compliant vehicular access / egress, drop-off, bike/courier and goods deliveries, fire access and refuse collection strategy.
- Provision for building and building services maintenance vehicular access, bicycle parking, motorcycle parking and EV charging is required.
- A coordinate waste strategy, refuse rooms, chutes (if any), recycling requirements, loading and BOH circulation with the base-building planning.
- Internal markings, finishing, wayfinding and lighting to the car parking should reflect a premium address and building.

Client Design Requirements and Residential Specifications

The following client requirements are to be treated as core briefing information and translated into coherent design principles, apartment typologies, room data requirements, outline specifications, façade strategy and shared-area design. Where authority, code, buildability or commercial constraints create tension with the brief, the architect shall identify options and recommendation notes rather than omit the requirement.

Apartment Planning and Spatial Quality

- Floor-to-ceiling windows to maximise light and views.
- Minimum floor-to-ceiling target of 3.2 m, subject to full services coordination and code compliance.
- Sliding doors with as seamless a threshold as practical to balconies.
- Choice testing for open and closed kitchen options where commercially and spatially viable.
- Good storage provision throughout apartments.
- Master bedroom layouts include bath and shower, with walk-in closet where achievable. Integrate dressing- table with theatre style lighting.

- Integrated ceiling lights in living spaces/bedrooms.
- All units have separate laundry room or cupboard.
- Provision for sliding doors to utility areas, bathrooms and pantries.

Residential Finishes and Joinery

- Fitted wardrobes.
- Porcelain floor tiles (preferably RAK Ceramics) (min size tbc)
- Painted walls.
- Wood-effect entrance door.
- Veneer-finished internal doors.

Kitchens, Appliances and Utilities

- Modern contemporary designed units (colour or wood finish)
- Wall units with integrated LED downlighting above work surfaces.
- Consider under counter integrated fridge/freezer drawer solution for larger units.
- Granite or stone worktops.
- Kitchen islands incorporating bar seating and cooking hob where unit planning allows. Integrate power sockets below counter or as a pop-up. Pop-up extractor unit for hob. Provision for downlights or pendants above.
- White goods preference: Franke.
- Central gas provision, subject to statutory acceptability and coordinated utility strategy.
- Water filters.
- Sink and drainer unit.
- Dishwashers for all unit types. Half-size for 1 bed.
- Waste disposal unit in sink, subject to MEP / drainage / FM review.
- Touch opening/ self-closing doors and drawers.
- Fitted appliances to be integrated at working levels at waist height or above.
- Separate utility room/pantry for 2beds and above.
- Downlighting

Bathrooms and Wellness Features

- Rain-effect showers.
- Wet-room effect to showers where feasible and durable.
- Chrome sanitary fittings and accessories (Kludi or similar).
- Bathroom storage and practical vanity solutions.
- Part-tiled with careful integration of feature finishes.
- Hair-dryer and shaving points.
- Master bathroom to include separate bath and shower where unit planning supports it.
- Backlit mirrors or units.
- Magnifying mirror element.
- Spotlighting above shower and sink units.

MEP & Smart Home Requirements

- Smart home technology provision throughout all units.
- Bluetooth thermostats in each room.
- Integrated ambient lighting (soft tone) throughout.
- Integrated sound system in living spaces.
- Automated blinds/curtains.
- Phone charging points in living areas.
- Brushed-effect sockets and switches in every room.

- Place sockets near beds for table lamps, alarms and charging. Above skirting in living areas and above worktops in kitchen.
- Coded security access system for front doors.

Balconies and External Interfaces

- Balcony lights.
- Glass-panel balcony balustrades.
- External power point on balcony.
- Balcony rain drainage provision.
- Privacy screens between balconies to prevent overlooking and acoustic controlled.
- Dimensions should be sufficient to accommodate garden furniture/outside dining sufficient for the level of occupancy.

Common Areas

- Light colour palette to corridors and lift lobbies.
- Common parts to express a premium but durable character aligned with the wider project positioning.
- The main lobby to be double or triple height using a maximum of 3 material types and colour palette.
- The reception area and desk should reflect Uniestate's brand identity.
- Consider a dedicated area or room for residents' lockers to accommodate parcel deliveries.
- Visitor's waiting area to contain soft furnishings and designed to reflect the look and feel of the building.
- Internal lighting to be soft and warm.
- Passenger lifts interior design to reflect the design elements and colour scheme for the lobbies and corridors.
- Consider a feature element – e.g. sculpture, artwork, plant/tree, water or lighting element.

Building Services and External Envelope

- Main pedestrian entrance and drop-off to be at street level. Building name to be clearly visible and lit. Materials used should compliment the design charter and reflect the client's brand identity.
- BMS for ongoing facilities and property management. The client will be providing concierge services in addition.
- Energy saving HVAC system independently metered per unit.
- Building to have Landlord's metering
- District cooling provided to the plot by Master Developer.
- Recycled grey water for irrigation to landscaped areas.
- Energy saving devices to be suggested where physically and feasibly possible.
- Façade elements to be contemporary design, easy to maintain and comply with the latest fire and safety regulations.
- Balconies to provide natural shading for glazed or overly exposed heat absorbent areas.
- Provision of sufficient lifts to service a tall residential building and in compliance with local planning and fire safety regulations.
- Separate goods lift or combined passenger and goods lift for operator deliveries and residents' furniture deliveries and removals.
- Cradle cleaning system with housing on the roof
- Mechanical floor at mid-level floor within the tower.
- Roof MEP, plant and equipment to be housed or shaded where possible.
- External lighting to tower and podium to comply with client design guidelines and should reflect the style of the brand.
- Ensure rainwater drainage and run-off is angled away from the building and away from door openings and thresholds at balcony interfaces.
- Drainage channels to be integrated and covered with filter systems easily accessible for cleaning & maintenance.

Landscaping

- Create a garden feel for the podium roof with sustainable planting including trees, shrubs and ground cover. Provide a mix of drought resistant plants and shrubs with tropical plants, which benefit from canopy shading.
- Create shaded seating and play areas through planting or sun resistant fabrics.
- Usable and accessible roof areas should provide areas for container planters to act as screening or areas of privacy around sun decks or pools.

Nb. A Client's Design Charter will be provided to the appointed LDC at project kick-off.

Statutory, Code and Technical Compliance Requirements

Without limiting the LDC's obligations, the design shall be developed to satisfy the current statutory and technical requirements applicable to the project, including but not limited to:

- Abu Dhabi building permit and code compliance requirements as administered by the Department of Municipalities and Transport and the relevant municipality / digital permit systems.
- Applicable Estidama / Pearl Building Rating System requirements and municipal sustainability submission procedures.
- Current UAE Fire and Life Safety Code of Practice requirements and Abu Dhabi Civil Defence review / approval requirements.
- The Najmat Master developer Control Plan.
- All utility authority requirements for power, water, drainage, telecoms, gas (if adopted), district cooling (if applicable), and any infrastructure interface obligations.
- Universal accessibility, life safety, vertical transportation, façade performance, emergency egress and occupancy certification requirements.
- Any handover, completion and building occupancy requirements necessary to achieve lawful occupation and operation.

Annex A – Land & Title Information

Land Site Plan
مخطط أرض

Certificate No: 202585000097617

رقم الشهادة: 202585000097617


PROPERTY DETAILS			تفاصيل العقار
Zone	Al Reem Island	جزيرة الريم	المنطقة
Sector	RRS	الريم 5	الحوض
Land area	3087.12 m2/ 33229.48 ft2		مساحة الأرض
Land No.	C3		رقم الأرض
Construction status	Not Constructed	غير مبني	حالة البناء
Allocation type	Residential	سكني	مسمى التخصيص
Land use	commercial-residential	تجاري-سكني	استخدام الأرض


Owner Details					معلومات المالك
Share and Acquisition الحصة والحيارة	Right Hold Type نوع الحق	Nationality/Source الجنسية / المصدر	EID /License No/ Passport No رقم الهوية / الرخصة / جواز سفر	Name الاسم	#
(100% Allotment) (100% منحة)	Freehold ملكية عقار حيازة مطلقة	NA لا يوجد	CN-1087020	REEM DEVELOPERS - SOLE PROPRIETORSHIP L.L.C. ريم للتطوير - شركة الشخص الواحد ذ م م	1

Land Site Plan مخطط أرض

Certificate No: 202585000097617


رقم الشهادة: 202585000097617

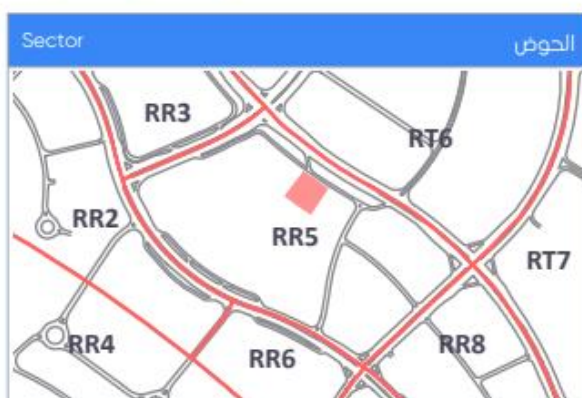

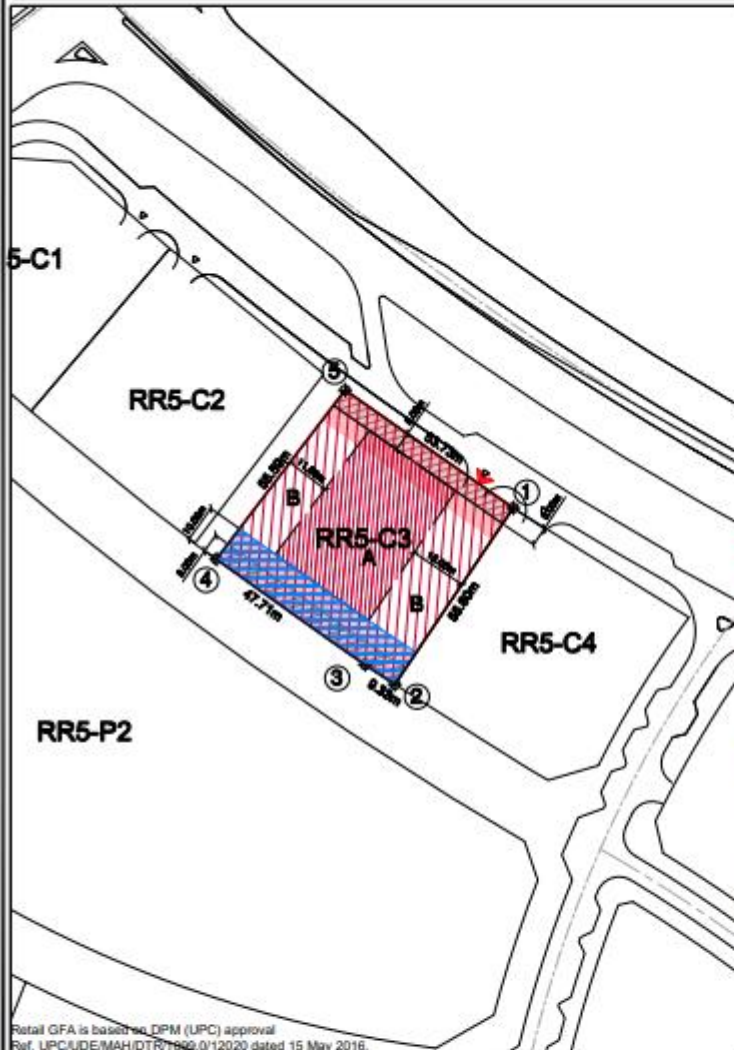

General Location

الموقع العام



KEY PLAN

خطة الموقع

- LEGEND:**
- Plot boundary
 - Podium Zone
 - Tower Zone
 - Open Space
 - Permissible Amenities Zone
 - Setback Zone
 - Retail Zone (indicative)
 - Radius
 - CL
 - Curve length
 - Intersection point, with numbers
 - Vehicular Access
 - Access for Emergency Vehicles
 - Townhouse Zone

- Notes:**
- Plans for illustration only - do not scale
 - For dimensions and locations refer to coordinate table
 - Levels relate to New Abu Dhabi Datum
 - Grid Data, Spheroid-Clarke 1880, Projection-UTM Zone 38N Horizontal Datum-1980, Positional Accuracy = 5mm
 - Major GFA definition as per UPC letter ref. UPCDRT/GPM/000001 dated 29 Jan 2008
 - All DPM's Policies and Manuals are applicable
 - Peak Rating System (PRS) is applicable
 - All Government Agency NOCs including DPM must be obtained
 - Traffic Impact Study (TIS) is to be submitted & approved by DOT
 - Plot vehicle access and parking shall be as per DOT TAP approval

COORDINATE TABLE			
Point	East	North	Levels
1	237466.871	2710321.514	-
2	237435.887	2710275.346	-
3	237428.120	2710280.525	-
4	237389.195	2710308.103	-
5	237422.866	2710352.343	-

Retail GFA is based on DPM (UPC) approval
Ref. UPC/IDE/MAH/DTR/1999.0/12020 dated 15 May 2016.
SCALE: 1:1000

Owner's Name: REEM DEVELOPERS		ريم للتطوير	
Project Director: REEM DEVELOPERS	مدير المشروع	Plot No: C3	رقم القسيمة
Signature:	التوقيع	Sector: RR5	رقم الحوض
Date:	التاريخ	Plot Area: 3,087 sq.m (33,228.1 SF)	مساحة القسيمة
Consultant:	الاستشاري	TOTAL GFA: 32,900 sq.m (354,133 SF)	
Prepared by: Z.S.	الإعداد	Residential: 32,400 sq.m (348,751 SF)	
Date: 18 Feb 2021	التاريخ	Office: -	
Rev: 7	المراجعة	Retail: 500 sq.m (5,382 SF)	
Checked by: J.H.	التدقيق	Community facilities: -	
DDC REF: RRS-C3-Rev7.dwg	رقم الوثيقة		

Land Use: Residential / Retail		استخدام الأرض	
Tower: A	برج	No. of Floors: 32-34	عدد الطوابق
Podium: B	مسطح	No. of Floors: 3	عدد الطوابق
Height: 136 m (Including Podium)	الارتفاع	Parking No: As per DOT requirements	عدد المواقف
		Max No. of Units: 250	أقصى عدد وحدات

"Where this Plot Plan is subject to formal approval by the Competent Authority it has been prepared in good faith, and no representation or warranty, express or implied, is or will be made and no responsibility or liability is or will be accepted by the Seller, in relation to the accuracy or completeness of this Plot Plan and any such liability is expressly disclaimed."

Annex B – Najmat Master Development Plan

Please see separate attached pdf file for the Najmat Masterplan containing Development Codes, Building Design Regulations and Guidelines.

Appendix B - Deliverables Matrix

Stage / workstream	Minimum deliverables	Format	Tenderer compliance / comments
Inception	Project execution plan, design management plan, CDE/BIM plan, programme, risk register, document register, approvals route map, information request.	PDF + native editable files as applicable	[Comply / qualify]
Pre-concept / massing	Minimum 3No options, area schedules, planning compliance, engineering feasibility, commercial comparison, approvals risk and recommended option.	PDF + native editable files as applicable	[Comply / qualify]
Concept architecture	Plans, elevations, sections, massing, facade concept, materials intent, accessibility, code strategy and presentation deck.	PDF + native editable files as applicable	[Comply / qualify]
Concept engineering	Structural, MEP, civil/infrastructure, utilities, fire strategy, traffic/parking and sustainability concepts.	PDF + native editable files as applicable	[Comply / qualify]
Concept landscape / lighting / signage	Landscape concept, public realm strategy, external lighting concept, wayfinding/signage hierarchy and master developer interface.	PDF + native editable files as applicable	[Comply / qualify]
Schematic design	Coordinated discipline drawings, calculations, reports, models, authority submission packages and cost plan coordination inputs.	PDF + native editable files as applicable	[Comply / qualify]
Detailed / tender design	Coordinated tender drawings, specifications, schedules, reports, models, design criteria, authority drawings and tender issue register.	PDF + native editable files as applicable	[Comply / qualify]
Authority approvals	Weekly tracker, submission logs, comments/responses, approvals/NOCs, meeting minutes and risk dashboard.	PDF + native editable files as applicable	[Comply / qualify]
Market launch pack	Launch design pack, bank/funder technical pack, area schedule, marketing source information, approvals status and caveat schedule.	PDF + native editable files as applicable	[Comply / qualify]

Appendix C - Authority Approval Matrix

Tenderers shall complete this matrix and include it in their technical proposal. Add or delete rows to suit the Project.

Authority / Stakeholder	Approval / NOC	Submission contents	Stage	Target date	Status / Risk / Comments
Master Developer (Modon/REEM Developers)	Design NOC / guideline compliance	Concept, schematic, detailed design packs	All stages	[date]	[risk]
DMT/ADM/TAMM/ MePS	Project registration / building permit / certified drawings	Forms, drawings, calculations, appointment letters, approvals	Inception-tender	[date]	[risk]
Planning / DPA/ UPC authority	Detailed Planning Approval / circulation plan	DPA forms, planning drawings, area schedules	Concept/schematic	[date]	[risk]
Estidama / Sustainable Buildings	Pearl Design Rating	PQP documents, credits, modelling, submissions	Concept-tender	[date]	[risk]
AD Civil Defence / FLS	Fire-life-safety approval	Fire strategy, FLS drawings, calculations	Concept-tender	[date]	[risk]
ITC / roads / traffic	Access / traffic / parking NOC	Traffic impact, access drawings, parking strategy	Pre-concept-schematic	[date]	[risk]
TAQA/ ADDC/ADWEA Distribution / utilities	Power/water connection / load approvals	Load schedules, single lines, water demand, connection drawings	Concept-tender	[date]	[risk]
Sewerage / stormwater / irrigation	Connection NOCs	Drainage, stormwater, irrigation and network drawings	Concept-tender	[date]	[risk]
DoE / gas authority	Gas design approval / NOC if applicable	Gas layouts, calculations, safety documents	Schematic-tender	[date]	[risk]
Telecoms providers	Telecom NOC / network approval	Riser, containment, telecom room and network layouts	Schematic-tender	[date]	[risk]
EAD / environmental	Environmental permit / PER / EIA / CEMP if applicable	Screening, reports, environmental management plans	Early concept	[date]	[risk]
Waste authority	Waste strategy / collection approval	Waste storage, access and collection strategy	Concept/schematic	[date]	[risk]
Aviation / height	Height / crane / aviation NOC if applicable	Height drawings, coordinates, crane strategy	Pre-concept	[date]	[risk]
ADTA / heritage	Heritage / archaeology NOC if applicable	Site screening and reports	Pre-concept	[date]	[risk]
Signage /Public Realm	Signage / wayfinding / lighting approvals	Signage family, external locations, lighting integration	Schematic-tender	[date]	[risk]

Appendix D - Fee Schedule Template

Tenderers shall complete all tables. Add rows as required.

Stage	Deliverable Trigger	Fee AED	% of total	Assumptions	Payment milestone
Mobilisation / inception	[accepted deliverable]	[AED]	[%]	[insert]	[insert]
Pre-concept / massing options	[accepted deliverable]	[AED]	[%]	[insert]	[insert]
Concept design	[accepted deliverable]	[AED]	[%]	[insert]	[insert]
Schematic design	[accepted deliverable]	[AED]	[%]	[insert]	[insert]
Detailed / tender design	[accepted deliverable]	[AED]	[%]	[insert]	[insert]
Authority approvals management	[accepted deliverable]	[AED]	[%]	[insert]	[insert]
Market launch / bank pack	[accepted deliverable]	[AED]	[%]	[insert]	[insert]
Tender support optional	[accepted deliverable]	[AED]	[%]	[insert]	[insert]

Resource Schedule

Name	Role / Discipline	Company	Grade	Day Rate (AED)	Planned days	Total AED
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]
[insert]	[insert]	[insert]	[insert]	[insert]	[insert]	[insert]

Appendix E - Form of Tender

To: UNIESTATE

We, *[INSERT TENDERER NAME]*, having examined the RFP and all addenda, offer to provide the full design consultancy services for PLOT C3/RR5, AL REEM ISLAND, ABU DHABI, UAE in accordance with our technical and commercial proposal for the lump sum fee of AED *[INSERT]*, *[insert in Words]* exclusive/inclusive of VAT as stated in our proposal.

We confirm that our proposal remains valid for 120 days from the tender submission deadline.

We confirm that we have allowed for all services, resources, subconsultants, coordination, authority submissions and deliverables necessary to meet the RFP requirements, subject only to the qualifications expressly stated in our exceptions schedule.

We acknowledge the critical requirement for market launch readiness within six months of appointment and confirm that our proposed programme and resources are based on achieving this milestone.

We confirm that the person signing this Form of Tender is authorised to bind the tenderer.

Tenderer (Legal name)	
Authorised signatory	<i>[INSERT]</i>
Title	<i>[INSERT]</i>
Signature	<i>[INSERT]</i>
Date	<i>[INSERT]</i>
Company stamp	<i>[INSERT]</i>
